



BHS Construction Progress Report

May 28, 2010

The Countdown to Opening is.....65 Days

New Technology

Past construction progress reports have provided information on some of the new technologies that will be utilized in the new patient tower. An important part of this new technology will be the implementation of a centralized nurse call system. This new technology will represent a new model for nurse call in the new patient tower. All calls will be funneled to a single location, and from there, the appropriate level caregiver will be notified. This will decrease unnecessary steps for caregivers while providing better and more efficient patient care. Another feature in all patient rooms is the patient lift system. All rooms are equipped with patient lift tracks, which will accommodate the patient lift system. This system will assist in safe patient handling, and at the same time, protect the backs of caregivers.

The new Simulation Center, located on Level 2, represents the latest in simulation training technology. Sim Man technology simulates real time patient conditions and situations that require caregivers to respond to the event that is created within the control room located in the Center. Their responses are then evaluated and used for educational training and learning.

Tower Construction Update

Exterior work

- Placement of the base and binder material for the roadway reconstruction in front of the Tower will begin next week;
- Removal of the Turner jobsite trailers will begin next week;

Level 0

- Ceramic tile installation in lobby is completed;

Level 1

- All Central Sterile equipment is installed;

Level 2

- Final coat of finish paint being applied in all areas;
- General cleanup activities underway, including removal of floor protection in all areas;


Interior Renovations Update

- Renovation work continues on the Second Floor corridor in the North building outside of the ED, and in the South building corridor outside of the cafeteria;
 - Installation of new ceiling tiles, light fixtures, and wall protection in the corridor is now finished, with flooring replacement scheduled next;
- The final renovation work in the cafeteria in the servery area will take place from June 7 to June 14;
- Renovation work continues on the men's and women's restrooms located on the First Floor in the South building;

Campus Exterior update

- Work on the Brady Street entrance canopy continues;
 - New panels expected to arrive in two weeks, with the installation expected to take three weeks;
- Demolition of the existing Brady Street entrance "storefront" and floor tile will begin on June 7;
 - Installation of new "storefront" glass panels, and new walk off carpet, will take place from June 7 to June 28;
- New sidewalks will also be installed at the Brady Street entrance, with demolition and reconstruction taking place from June 7 to June 28;

PROJECT TIMELINE, MAY-AUGUST

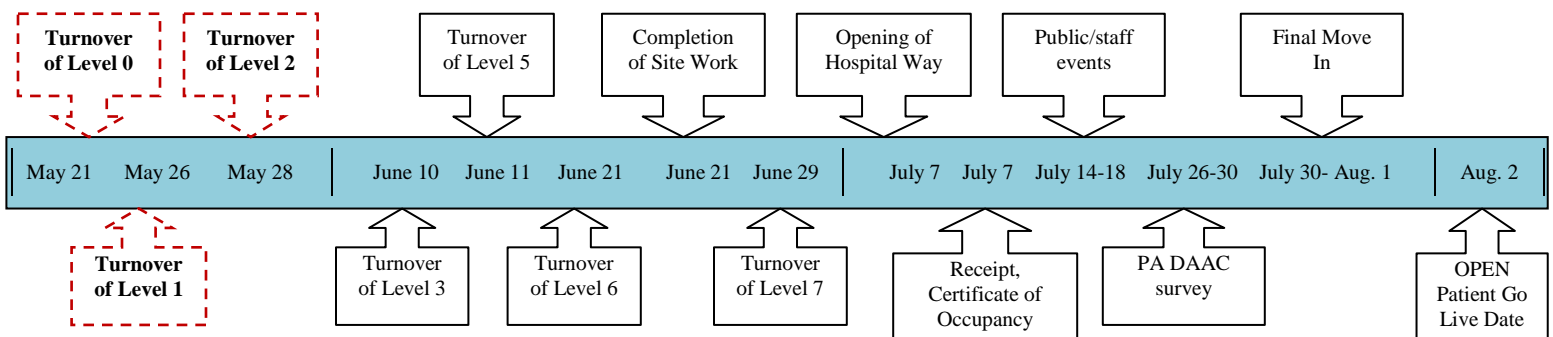

Questions about the project can be sent to towerinfo@butlerhealthsystem.org
